




# **PROVIDENCE FIBER NETWORK MONTHLY UPDATE**

**JANUARY 3, 2024**



## PROVIDENCE FIBER PROJECT MAP

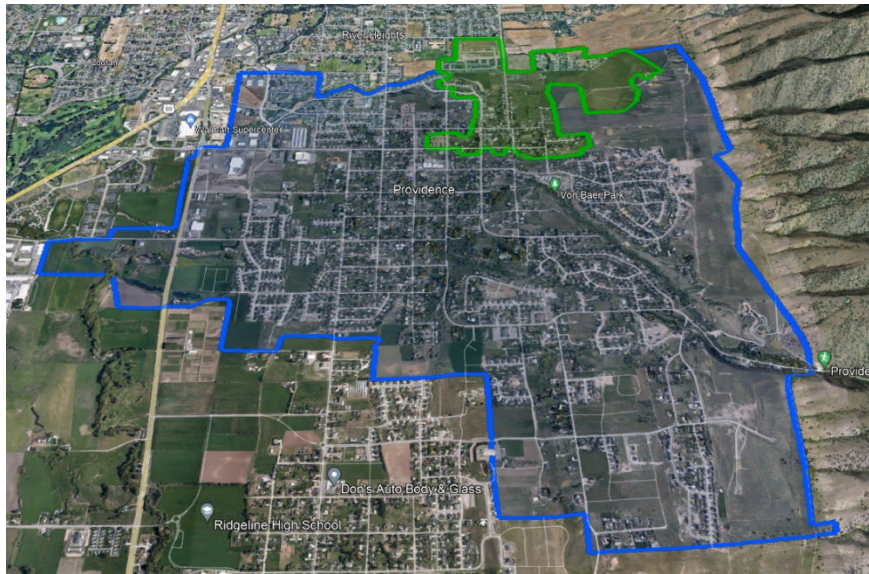

■ Complete  
■ In Progress

“Install was done in 45 minutes. The two technicians were very accommodating and ran the fiber right to my wiring hub under the stairs of the town home.”

“...The crews working on the project were very responsive, professional and thorough. I am excited for the opportunity to use this technology.”

## PROJECT OVERVIEW

### CONSTRUCTION AGREEMENT

24 February 2021

### START DATE

1 May 2021

### SUBSTANTIAL COMPLETION

20 April 2024

### MILESTONES COMPLETED SINCE LAST REPORT

- Zone 4 construction is complete and installations are in progress
- Service is now available to 2,910 households

### COMPLETED MAINLINE TRENCH


257,865 feet (100%)

## PROJECT STATUS BY ZONE

	Start Date	Mainline Construction	Fiber Placement	Fiber Splicing	Completed Drops	Installed ONT's	Scheduled Completion Date
Shelter	07.26.21						11.30.21
Zone 2	08.31.21	100%	100%	100%	613	398	12.02.22
Zone 1	11.08.21	100%	100%	100%	527	341	4.30.23
Zone 5	08.18.22	100%	100%	85%	246	118	1.15.24
Zone 3	11.01.22	100%	100%	100%	369	158	10.31.23
Zone 4	07.10.23	100%	100%	100%	404	34	12.26.23
TOTAL:					2159	1049	



## PROJECT COMPLETION TIMELINE

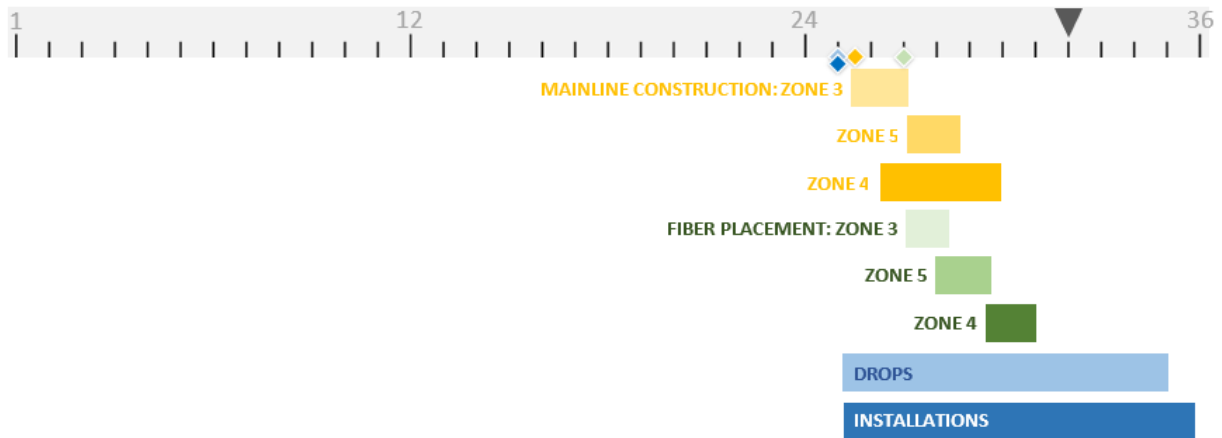

## ENGINEERING

### ENGINEERING PLANS/DRAWINGS

All MDU/HOA developments, except for Visionary Homes, have been coordinated.

### REDLINED CONSTRUCTION DRAWINGS

The recordkeeping process of posting redlined mainline construction and fiber is ongoing for zones 1, 3, 4, and 5. All mainline conduits, vaults, pedestals, and fiber have been recorded in Zone 2.

## CONSTRUCTION

	MAINLINE CONSTRUCTION	FIBER PLACEMENT, SPLICING AND TESTING	ONT INSTALLATIONS
Zone 1	COMPLETE	COMPLETE	In progress in all areas
Zone 2	COMPLETE	COMPLETE	In progress in all areas
Zone 3	COMPLETE	COMPLETE	In progress in all areas
Zone 4	COMPLETE	COMPLETE	In progress in all areas
Zone 5	COMPLETE	Currently wrapping up splicing and testing in subzone 5-3; projected to begin ONT installations the third week of January	In progress in subzone 5-1 and 5-2
FIBER DROPS		In progress in all zones	



## MARKETING/PUBLIC RELATIONS

### MAINLINE CONSTRUCTION ANNOUNCEMENT

This month our team worked to provide Providence City with a press release to celebrate the completion of mainline construction.

### EMAIL NOTIFICATION

We are also working on an email notification to residents who have previously received a drop but still need an in-home installation. The email will let residents know they are on their way to a fiber connection, but to receive the benefits of the network, they must select an ISP to complete their in-home installation.
